


## Data as of February 9, 2007

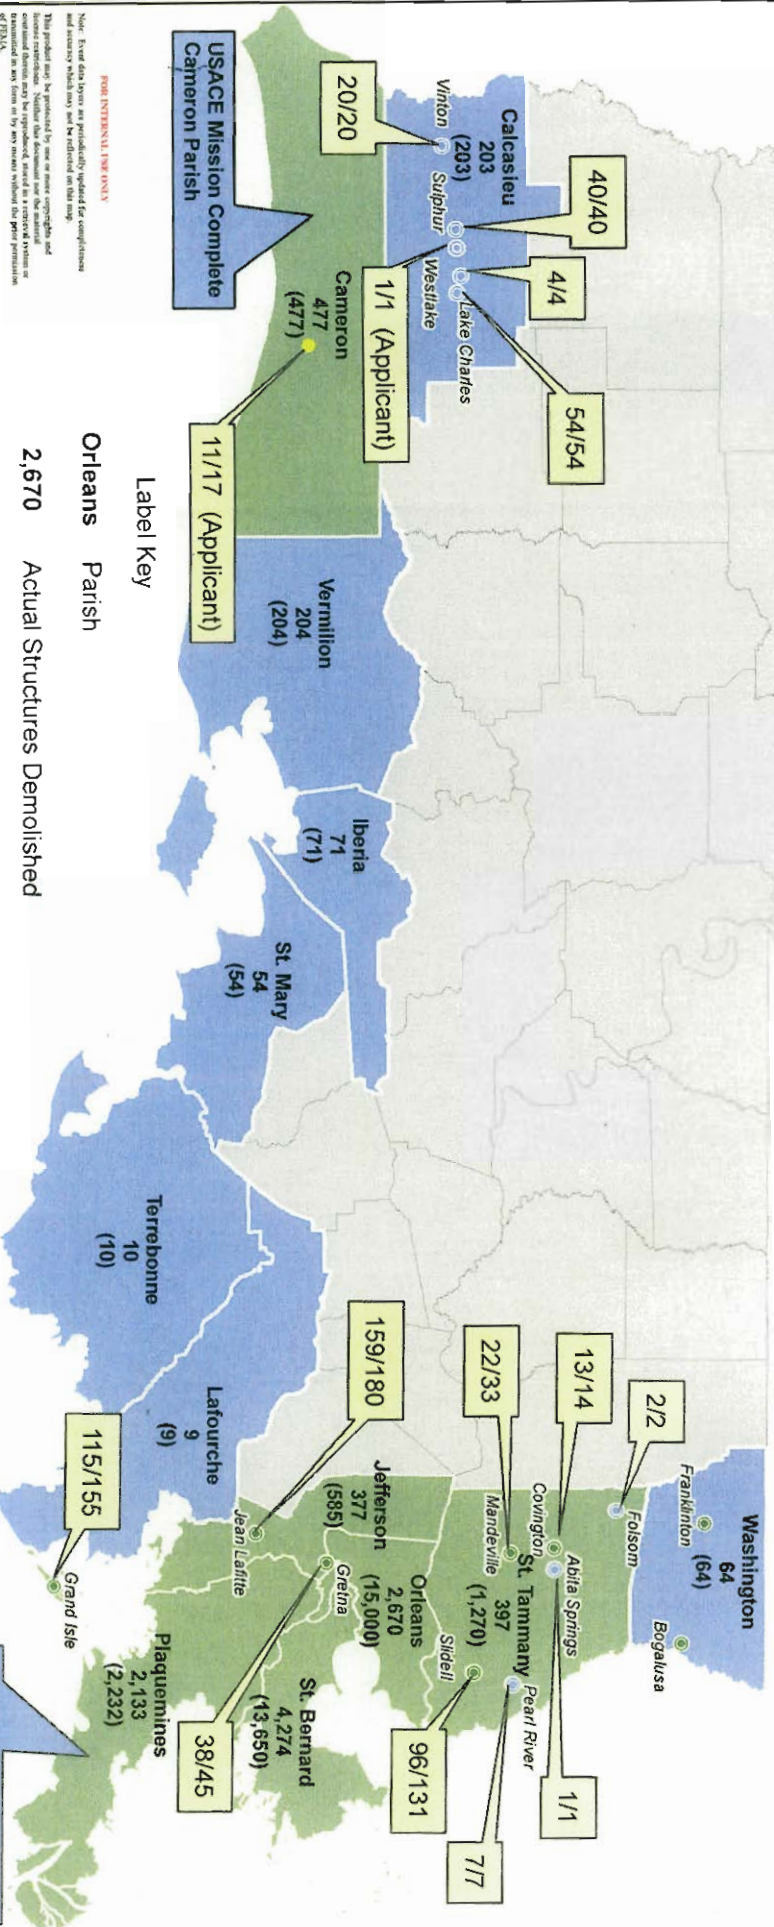

Label Key

Orleans Parish

2,670 Actual Structures Demolished

Estimated Structures  
(15,000)


Geospatial Intelligence Unit - LTRD  
Printed on 20070212  
M:DebrisDemolition Status20070212

## USACE Mission Complete Plaquemines Parish

# PPDR Status

Data as of February 09, 2007

- | City | Parish         |
|------|----------------|
|      | PPDR COMPLETED |
|      | PPDR APPROVED  |

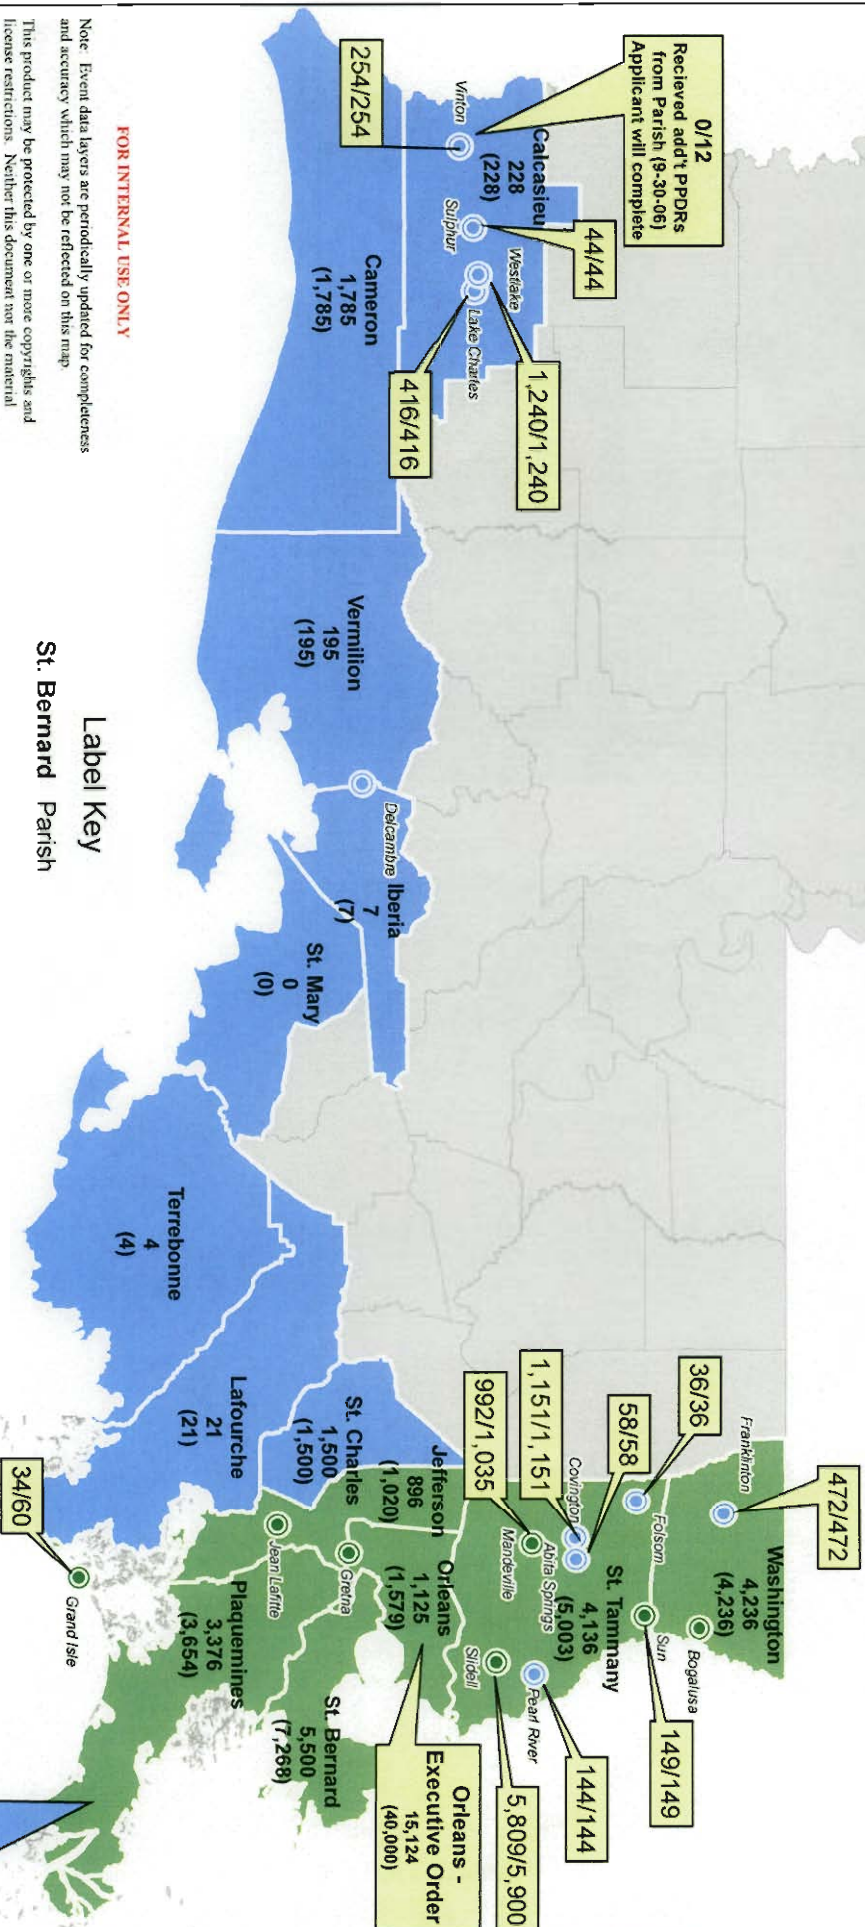

FOR INTERNAL USE ONLY

Note: Event data layers are periodically updated for completeness and accuracy which may not be reflected on this map.

This product may be protected by one or more copyrights and license restrictions. Neither this document nor the material contained therein may be reproduced, stored in a retrieval system or transmitted in any form or by any means without the prior permission of FEMA.


Label Key  
St. Bernard Parish

5,500 PPDR Completed

(7,268) PPDR Estimated



Data as of February 9, 2007

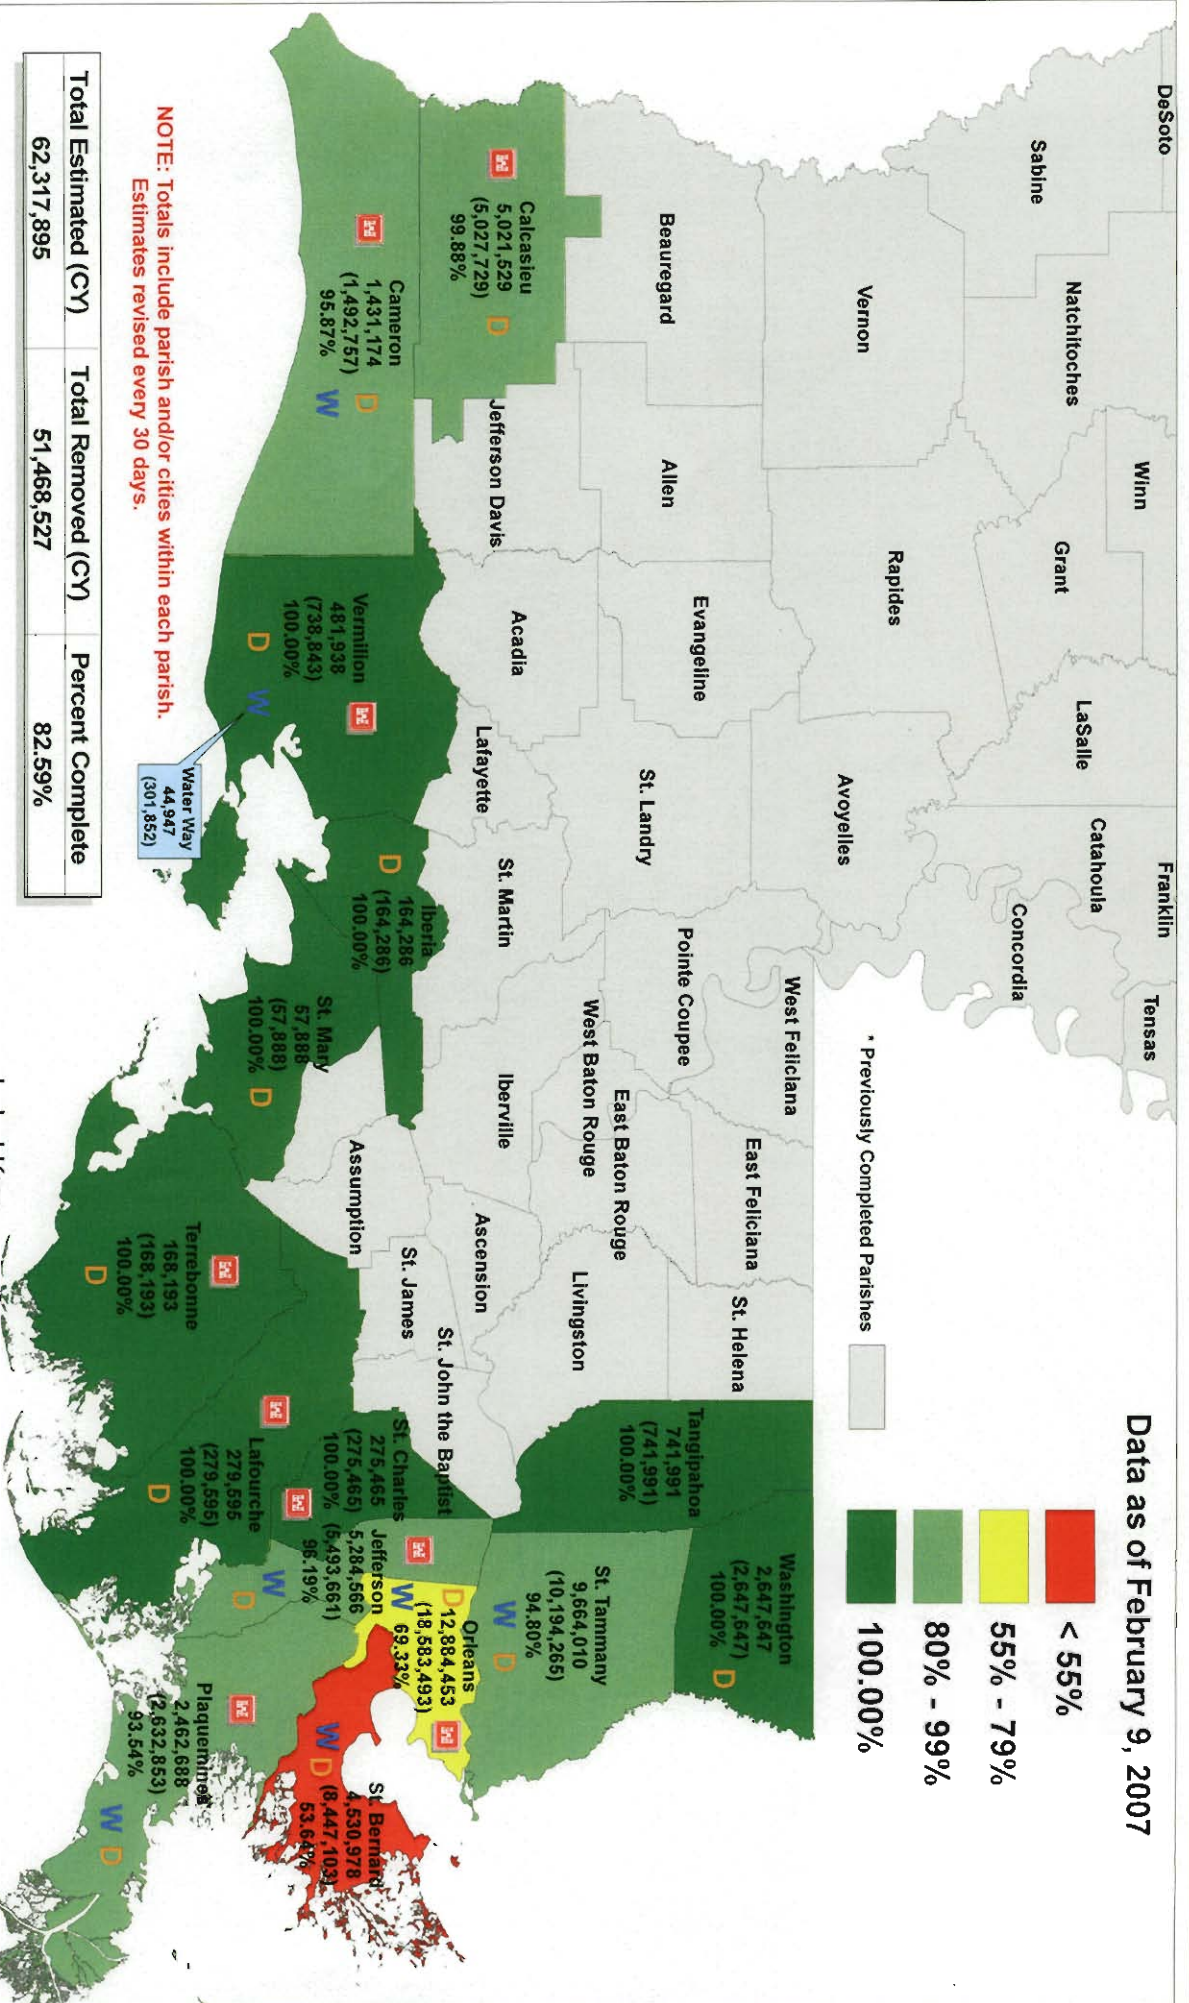



HQ Report		2/9/2007		1603 - Katrina					
USACE	Estimate (CY)	Actual (CY)	%Complete	Estimate Cost (\$/CY)	Estimated Removal Cost	Debris Removed Cost (\$/CY)			
Curbside	19,488,679	18,888,476	96.9%	\$40.00	\$779,547,160.00	\$755,539,040.00			
PPDR*	1,922,650	1,230,875	64.0%	\$40.00	\$76,906,000.00	\$49,235,000.00			
DEMO**	6,120,602	1,414,352	23.1%	\$40.00	\$244,824,080.00	\$56,574,080.00			
Waterways	124,203	124,203	100.0%	\$47.00	\$5,837,541.00	\$5,837,541.00			
Ditches	105,000	25,674	24.5%	\$47.00	\$4,935,000.00				
TOTALS	27,761,134	21,657,906	78.0%		\$1,112,049,781.00	\$867,185,661.00			
Applicant	Estimate (CY)	Actual (CY)	%Complete	Estimate Cost (\$/CY)	Estimated Removal Cost	Debris Removed Cost (\$/CY)			
Curbside	19,122,983	17,997,887	94.1%	\$40.00	\$764,919,320.00	\$719,915,480.00			
PPDR*	1,706,915	1,497,890	87.8%	\$40.00	\$68,276,600.00	\$59,915,600.00			
DEMO**	4,602,500	1,512,750	32.9%	\$40.00	\$184,100,000.00	\$60,510,000.00			
Waterways	58,370	52,263	89.5%	\$47.00	\$2,743,390.00	\$2,456,361.00			
Ditches	7,000	0							
TOTALS	25,497,768	21,060,790	82.6%		\$1,020,039,310.00	\$842,797,441.00			
USCG	Estimate (CY)	Actual (CY)	%Complete	Estimate Cost (\$/CY)	Estimated Removal Cost	Debris Removed Cost (\$/CY)			
Waterways	93,457	50,211	53.7%	\$81.00	\$7,570,017.00	\$4,067,091.00			
TOTAL of Katrina	53,352,359	42,768,907	80.2%		\$2,139,659,108.00	\$1,714,050,193.00			
1607 - Rita									
USACE	Estimate (CY)	Actual (CY)	%Complete	Estimate Cost (\$/CY)	Estimated Removal Cost	Debris Removed Cost (\$/CY)			
Curbside	6,214,760	6,214,760	100.0%	\$40.00	\$248,590,400.00	\$248,590,400.00			
PPDR	283,285	283,285	100.0%	\$40.00	\$11,331,400.00	\$11,331,400.00			
DEMO	291,074	291,074	100.0%	\$40.00	\$11,642,960.00	\$11,642,960.00			
Water Ways and Ditches	54,000	0	0.0%	\$47.00	\$2,538,000.00	\$0.00			
TOTALS	6,843,119	6,789,119	99.2%		\$271,564,760.00	\$271,564,760.00			
Applicant	Estimate (CY)	Actual (CY)	%Complete	Estimate Cost (\$/CY)	Estimated Removal Cost	Debris Removed Cost (\$/CY)			
Curbside	1,663,915	1,652,832	99.3%	\$40.00	\$66,556,600.00	\$66,113,280.00			
PPDR	134,400	133,200	99.1%	\$40.00	\$5,376,000.00	\$5,328,000.00			
DEMO	22,250	20,750	93.3%	\$40.00	\$890,000.00	\$830,000.00			
Water Ways and Ditches	301,852	44,947	14.9%						
TOTALS	2,122,417	1,851,729	87.2%		\$72,822,600.00	\$72,271,280.00			
*PPDR based on estimates									
**Demo based on estimates									
Total of Rita	8,965,536	8,640,848	96.38%	44,753,955	\$344,387,360.00	\$343,836,040.00			

62,317,895

51,409,755

TOTALS					
Parameter	Amount Expected (CY)	Amount to Date (CY)	Percent Complete	Target Date for Completion Rita/Katrina	Comment
USACE Debris	27,909,374	26,617,396	95.37%	Oct 06 / June 07	
Applicant Debris	22,628,213	21,281,809	94.05%	Nov 06 / Mar 07	
Waterways and Ditches (USACE & App Combined)	650,425	247,087	37.99%	Nov 06 /Dec 06	
Water Ways US Coast Guard	93,457	50,211		Mar 07	
USACE Demolition	6,411,676	1,705,426	26.60%	Oct 06 / Sept 07	
Applicant Demolition	4,624,750	1,533,500	33.16%	Nov 06 / May 07	St. Bernard = 10,000 structures, 25 structures/day. Total 13 months - 5/07
Totals	62,317,895	51,435,429	82.5%		
COST TOTAL		Total Estimated Removal Cost at \$40/CY & \$47/CY for waterways \$2,471,541,451		Debris Removed cost at \$40/CY &\$47/CY for waterways to date \$2,053,819,142.00	



1603 - Katrina							
USACE	Estimate (CY)	Actual (CY)	%Complete	Estimate Cost (\$/CY)	Estimated Removal Cost	Debris Removed Cost (\$/CY)	
Curbside	19,488,679	18,888,476	96.9%	\$40.00	\$779,547,160.00	\$755,539,040.00	
PPDR*	1,922,650	1,230,875	64.0%	\$40.00	\$76,906,000.00	\$49,235,000.00	
DEMO**	6,120,602	1,414,352	23.1%	\$40.00	\$244,824,080.00	\$56,574,080.00	
Waterways	124,203	124,203	100.0%	\$47.00	\$5,837,541.00	\$5,837,541.00	
Ditches	105,000	25,674	24.5%	\$47.00	\$4,935,000.00		
TOTALS	27,761,134	21,657,906	78.0%		\$1,112,049,781.00	\$867,185,661.00	
Applicant	Estimate (CY)	Actual (CY)	%Complete	Estimate Cost (\$/CY)	Estimated Removal Cost	Debris Removed Cost (\$/CY)	
Curbside	19,122,983	17,997,887	94.1%	\$40.00	\$764,919,320.00	\$719,915,480.00	
PPDR*	1,706,915	1,497,890	87.8%	\$40.00	\$68,276,600.00	\$59,915,600.00	
DEMO**	4,602,500	1,512,750	32.9%	\$40.00	\$184,100,000.00	\$60,510,000.00	
Waterways	58,370	52,263	89.5%	\$47.00	\$2,743,390.00	\$2,456,361.00	
Ditches	7,000	0					
TOTALS	25,497,768	21,060,790	82.6%		\$1,020,039,310.00	\$842,797,441.00	
USCG	Estimate (CY)	Actual (CY)	%Complete	Estimate Cost (\$/CY)	Estimated Removal Cost	Debris Removed Cost (\$/CY)	
Waterways	93,457	50,211	53.7%	\$81.00	\$7,570,017.00	\$4,067,091.00	
TOTAL of Katrina	53,352,359	42,768,907	80.2%		\$2,139,659,108.00	\$1,714,050,193.00	

1607 - Rita							
USACE	Estimate (CY)	Actual (CY)	%Complete	Estimate Cost (\$/CY)	Estimated Removal Cost	Debris Removed Cost (\$/CY)	
Curbside	6,214,760	6,214,760	100.0%	\$40.00	\$248,590,400.00	\$248,590,400.00	
PPDR	283,285	283,285	100.0%	\$40.00	\$11,331,400.00	\$11,331,400.00	
DEMO	291,074	291,074	100.0%	\$40.00	\$11,642,960.00	\$11,642,960.00	
Water Ways and Ditches	54,000	0	0.0%	\$47.00	\$2,538,000.00	\$0.00	
TOTALS	6,843,119	6,789,119	99.2%		\$271,564,760.00	\$271,564,760.00	
Applicant	Estimate (CY)	Actual (CY)	%Complete	Estimate Cost (\$/CY)	Estimated Removal Cost	Debris Removed Cost (\$/CY)	
Curbside	1,663,915	1,652,832	99.3%	\$40.00	\$66,556,600.00	\$66,113,280.00	
PPDR	134,400	133,200	99.1%	\$40.00	\$5,376,000.00	\$5,328,000.00	
DEMO	22,250	20,750	93.3%	\$40.00	\$890,000.00	\$830,000.00	
Water Ways and Ditches							
TOTALS							
TOTALS	2,122,417	1,651,729	87.2%		\$72,822,600.00	\$72,271,280.00	
PPDR based on estimate	355,852	355,852					
**Demo based on estimates							
Total of Rita	8,965,536	8,640,848	96.38%	44,753,955	\$344,387,360.00	\$343,836,040.00	

62,317,895                      51,409,755

TOTALS					
Parameter	Amount Expected (CY)	Amount to Date (CY)	Percent Complete	Target Date for Completion Rita/Katrina	Comment
USACE Debris	27,909,374	26,617,396	95.37%	Oct 06 / June 07	
Applicant Debris	22,628,213	21,281,809	94.05%	Nov 06 / Mar 07	
Waterways and Ditches (USACE & App Combined)	650,425	247,087	37.99%	Nov 06 /Dec 06	
Water Ways US Coast Guard	93,457	50,211		Mar 07	
USACE Demolition	6,411,676	1,705,426	26.60%	Oct 06 / Sept 07	
Applicant Demolition	4,624,750	1,533,500	33.16%	Nov 06 / May 07	St. Bernard = 10,000 structures, 25 structures/day. Total 13 months - 5/07
Totals	62,317,895	51,435,429	82.5%		
COST TOTAL		Total Estimated Removal Cost at \$40/CY & \$47/CY for waterways \$2,471,541,451		Debris Removed cost at \$40/CY & \$47/CY for waterways to date \$2,053,819,142.00	
