



Shaw Environmental & Infrastructure, Inc.

Shaw Environmental & Infrastructure, Inc.

4171 Essen Lane
Baton Rouge, LA
225 932-2500
FAX: 225-987-7300

April 10, 2007

Project No.: 123926
HAND DELIVERED

Mr. Keith Casanova, Administrator
Remediation Services Division
Department of Environmental Quality
P. O. Box 82178
Baton Rouge, LA 70884-2282

RE: Monthly Report – February 2007
7700 Earhart Boulevard Facility
New Orleans, Louisiana
Agency Interest Number 1275

Dear Mr. Casanova:

On behalf of T H Agriculture and Nutrition, L.L.C. (THAN) and Elementis Chemicals, Inc (Elementis – formerly Harcros Chemicals, Inc.), Shaw Environmental & Infrastructure, Inc. is submitting this monthly project status report for the month of February.

Should you have any question please contact me at (225) 389-4116.

Sincerely,
Shaw Environmental & Infrastructure, Inc.

Mike Hebert
Project Manager

cc: Mr. Larry LeJeune – LDAF (2 copies)
Mr. Jack Cleary – THAN (1 copy)
Mr. Glen Cavanaugh – Elementis (1 copy)
Mr. Dwayne Johnson - Kean, Miller, et al. (1 copy)
Mr. Mike Potts – Environ (1 copy)
Project Files – (2 copies)



Remediation Services Division	
Manager:	<i>Hebert</i>
Team Leader:	<i>Amphora</i>
AI #:	<i>1275</i>
TEMPO Task #:	<i>2385262</i>
<input checked="" type="checkbox"/> Desk Copy	<i>File Room</i>

Monthly Project Status Report

PERIOD: FEBRUARY 2007
PREPARED BY: SHAW ENVIRONMENTAL & INFRASTRUCTURE, INC.
7700 EARHART BLVD. FACILITY
NEW ORLEANS, LOUISIANA

1. Activities

Excavated Area 1-B and 1-C. Continued off-site storm drain cleaning.

2. Summary of Field Activities

Week of 02/01/07:

- SEMS moved ERAB and began excavation in Area 1-B.
- Shaw conducted confirmatory soil sampling and air monitoring using a photoionization detector (PID), as required.
- Clean Harbors removed full roll-off boxes for transportation to the TSD facilities and delivered additional empty containers.

Week of 02/05/07:

- SEMS completed excavation in Area 1-B.
- Shaw conducted confirmatory soil sampling and air monitoring using a (PID), as required.
- Clean Harbors removed full roll-off boxes for transportation to the TSD facilities and delivered additional empty containers.
- Surveyors documented excavation limits and sampling location in Area 1-B.
- ICI completed sewer cleaning along Burdette between Earhart and Colapissa; then began cleaning the Lowerline section; the section along Burdette from Colapissa to Fig was then completed.

Week of 02/12/07:

- Confirmatory samples from Area 1-B indicated that all samples were below their respective remedial action levels (RALs), except one side-wall sample in the former tankhold area.
- SEMS simultaneously began backfilling in the clean section of Area 1-B and over-excavating the former tankhold area.
- Shaw re-sampled the area that required excavation over the initial limits.

Week of 02/19/07:

- Confirmatory samples from the former tankhold area, that required further excavation, indicated that over excavation of the initial limit met the goals of the RALs.
- SEMS moved the ERAB and began excavation in Area 1-C.
- Clean Harbors transported ten thousand (10,000) gallons of contact water to Deer Park, TX.

- Clean Harbors also continued transporting roll off boxes off site.
- Shaw conducted air monitoring, as required.

Week of 02/26/07:

- SEMS completed excavation in Area 1-C, including the area surrounding MW-5S.
- In addition to the normal daily air monitoring, Shaw collected air samples using SUMMA canisters, both inside and outside of the ERAB, for analysis.
- Clean Harbors also continued transporting roll off boxes off site.

3. Summary of Sampling and Analysis During this Reporting Period

- Air sampling was performed in accordance with the plan.
- Confirmatory soil sampling was conducted to confirm excavation was completed to the proper extent.
- Surveying was conducted to document the limits of excavation and soil sampling locations.

4. Summary of Changes Made During this Reporting Period

- None.

5. Summary of Problems During this Reporting Period And Resolution

- None.

6. Waste Shipments

- Sixty-six (66) roll-off boxes of soil were shipped to Deer Park, TX for incineration.
- Five (5) roll-off boxes of debris were shipped to Lone Mountain, OK for microencapsulation.
- Thirty thousand (30,000) gallons of liquids were shipped to Deer Park, TX for incineration.

7. Projected Work for Next Reporting Period (March 2007)

- Continue soil and underground facilities removal.

8. Other

- None.

9. Site Visitors

- LDEQ personnel present weekly.

Photolog



Photo No. 01 ERAB moved into position over Area 1-B, from clean excavation Area 1-A.



Photo No. 02 Former tankhold excavation area.

Photolog

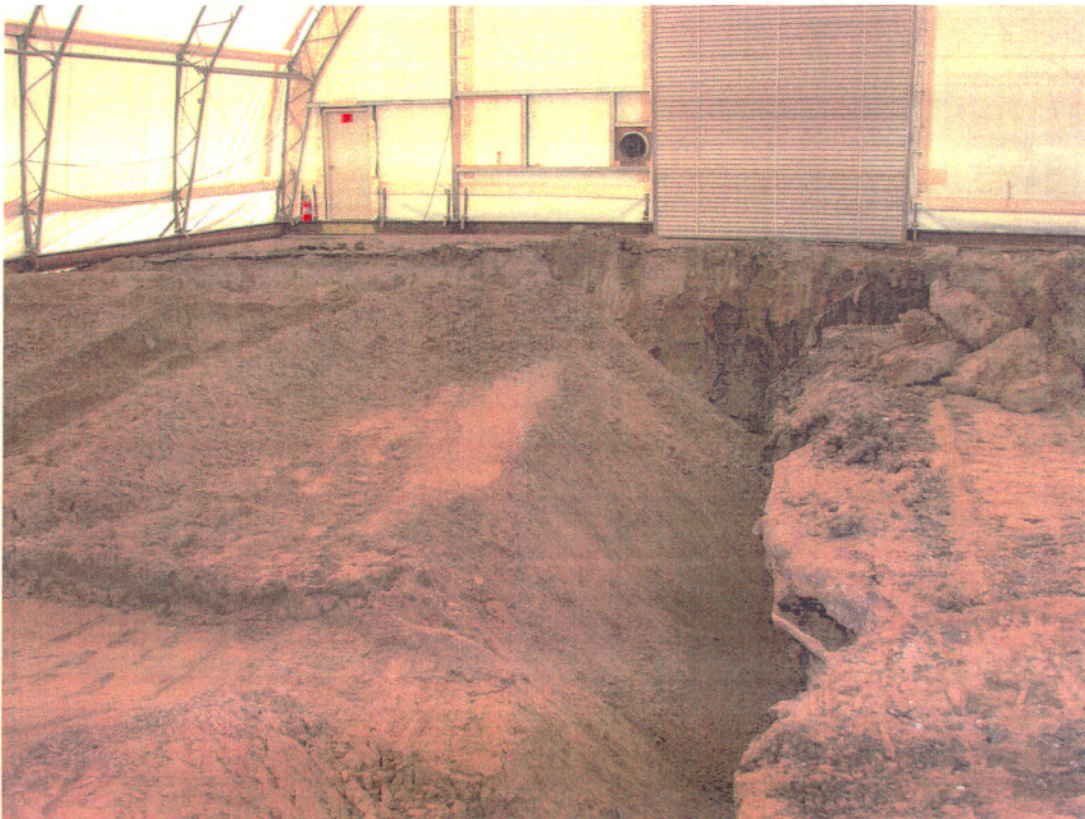


Photo No. 03 Backfilling Area 1-B.



Photo No. 04 ERAB moved into position over Area 1-C, from clean excavation Area 1-B.



Photo No. 05 Excavation in Area 1-C.



Photo No. 06 Monitoring well (MW-5S) excavation area.



Photo No. 07 Liquids from MW-5S.



Photo No. 08 Surveying excavation limits.
