



January 19, 2007

Project No.: 123926
HAND DELIVERED

Mr. Keith Casanova, Administrator
Remediation Services Division
Department of Environmental Quality
P. O. Box 82178
Baton Rouge, LA 70884-2282

RE: Monthly Report - December 2006
7700 Earhart Boulevard Facility
New Orleans, Louisiana
Agency Interest Number 1275

Dear Mr. Casanova:

On behalf of T H Agriculture and Nutrition, L.L.C. (THAN) and Elementis Chemicals, Inc (Elementis – formerly Harcros Chemicals, Inc.), Shaw Environmental & Infrastructure, Inc. is submitting this monthly project status report for the month of December.


Should you have any question please contact me at (225) 389-4116.

Sincerely,
Shaw Environmental & Infrastructure, Inc.

A handwritten signature in black ink, appearing to read "Mike Hebert", is written over a light blue grid background.

Mike Hebert
Project Manager

cc: Mr. Larry LeJeune – LDAF (2 copies)
Mr. Jack Cleary – THAN (1 copies)
Mr. Glen Cavanaugh – Elementis (1 copies)
Mr. Dwayne Johnson - Kean, Miller, et al. (1 copy)
Project Files – (2 copies)



Remediation Services Division	
Manager:	<i>Hebert</i>
Team Leader:	<i>Arriagosa</i>
AI #:	<i>1275</i>
TEMPO Task #:	<i>2333596</i>
<input checked="" type="checkbox"/> Desk Copy	<input type="checkbox"/> File Room

Monthly Project Status Report

PERIOD: DECEMBER 2006
PREPARED BY: SHAW ENVIRONMENTAL, INC.
7700 EARHART BLVD. FACILITY
NEW ORLEANS, LOUISIANA

1. Activities

Enclosed Remedial Activities Building (ERAB) and associated air handling equipment construction, monitoring well plugging and abandonment (P&A) and general site wide activities associated with completion of the building demolition and preparation of the soil excavation scope of work.

2. Summary of Field Activities

The week of 12/1/06 Southern Environmental Management and Specialties (SEMS) cleaned the former warehouse area and other key areas on-site and continued construction of the ERAB.

The week of 12/4/06 the crew from SEMS continued to assemble the ERAB. Industrial Cleanup, Inc. (ICI) removed the remaining warehouse debris and transported it to Waste Management for disposal. ICI also began working on the air handling unit for the ERAB. Pro-Tech P&A the eight on-site monitoring wells. Shaw personnel installed the on-site meteorological station. All Purpose Communications installed the video camera system in the ERAB (two of the four were installed this week). A New Orleans Department of Public Works representative visited the site to discuss the plan for cleaning storm drains. There was also a status meeting on-site for personnel from Shaw and THAN representatives.

The week of 12/11/06 SEMS continued working on the ERAB. Placement of the exterior fabric was finalized and SEMS began working on the doors and other openings. By week's end the ERAB was moved into position for the first excavation area along Colapissa St. and the air treatment system was put in place adjacent to the ERAB. SEMS also brought a bob tail roll-off truck on site to move boxes over when excavation activities begin. Shaw Safety personnel visited the site for a safety inspection and to check work progress. Clean Harbors visited the site as well. The decontamination trailer was set-up on-site and the surveillance camera installation was completed. All Purpose Communications completed the camera installation. The scales for trucks hauling roll-off boxes were also installed.

The week of 12/18/06 activities were focused on making final preparation for beginning excavation. The excavator to be used in the ERAB was delivered. A Shaw survey crew marked out the areas of remediation and several previous sample locations. SEMS built a supplied air bottle rack for the excavator, installed duct work for the air filtration system and sealed the exterior of the ERAB, among other final details. The New Orleans Fire Department visited the site to inspect the ERAB and a certificate of occupancy was granted.

The week of 12/26/06 the SEMS crew worked on staging equipment around the site and continued sealing the ERAB. The air monitoring documents were reviewed to ensure all was in place and the breathing air system was constructed. Shaw personnel worked on plans for implementing the air monitoring procedure.

3. Summary of Sampling and Analysis During this Reporting Period

Collected building material samples for analysis.

4. Summary of Changes Made During this Reporting Period

None.

5. Summary of Problems During this Reporting Period And Resolution

None.

6. **Waste Shipments**

1 roll-off box filled with general construction debris to River Birch Landfill.

7. **Projected Work for Next Reporting Period (January 2007)**

Excavation.

8. **Other**

None

9. **Site Visitors**

LDEQ present weekly

N.O. Department of Public Works

N.O. Fire Department

- Distribution List:
Keith Casanova, LDEQ
Larry LeJeune, LDAF
Mike Hebert, Shaw
Jack Cleary, THAN
Glen Cavanaugh, Elementis
Dwayne Johnson, Kean Miller, et al.
Site Files
Shaw Project Files (BR)

Location: New Orleans

Photographer:

Project No.: 123926

Client: THAN

Date: December 2006

Direction:

Description:

ERAB frame construction.



Direction:

Description:

Placement of ERAB shell.



Location: New Orleans

Photographer:

Project No.: 123926

Client: THAN

Date: December 2006

Direction:

Description:

Assembly of ERAB openings.



Direction:

Description:

Connection of air treatment system.



Location: New Orleans

Photographer:

Project No.: 123926


Client: THAN

Date: December 2006

Direction:

Description:

Monitoring well P&A.

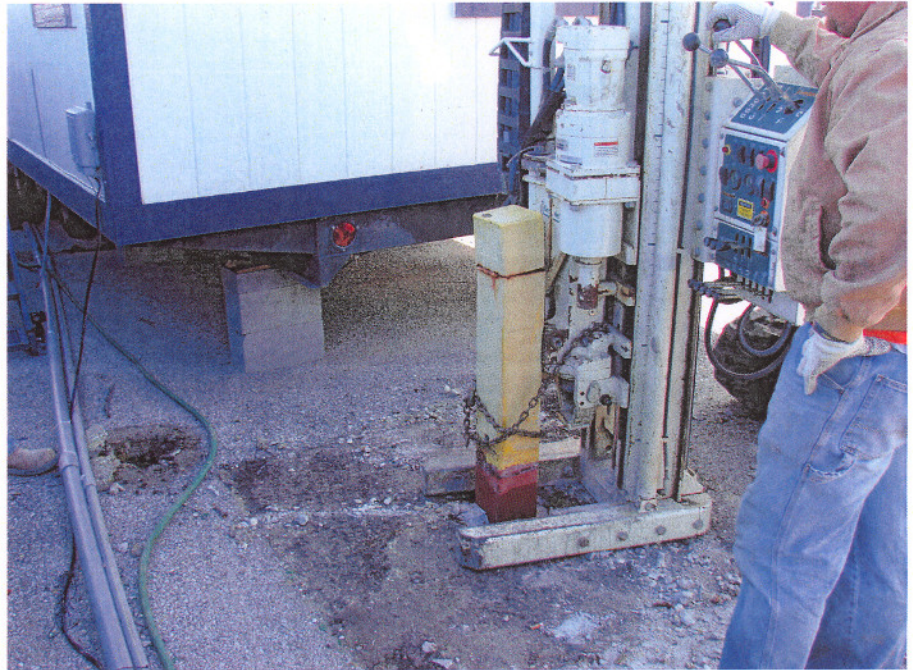

Direction:

Description:

Monitoring well P&A.

